

SAP Implementation Project **(ASAP Methodology)**

Agenda

- History and importance of ASAP methodology
- Detailed explanation of each phase in Implementation
- Roles of consultants in different phases of Implementation
- Explaining the documents used in Implementation with sample documents

History of ASAP Methodology

- By the mid 1990s, SAP procedures got a significant amount of negative publicity related to some high profile disasters. Though the companies knew that the ends were inevitable, SAP was criticized of being complicated, expensive and required long delivery schedules
- This is when SAP came up with its ASAP roadmap to sort out the numerous SAP projects that were over budget, over time and were at the risk of failure
- The ASAP (Accelerated SAP) methodology provides the roadmap for optimizing and continuous implementation of SAP systems in business processes
- The ASAP roadmap also includes various ITIL (Information Technology Infrastructure Library) elements and Value SAP techniques to make project solutions more robust, cost effective, timely and successful
- The roadmap brings in a multiple number of tools, information and accelerators to assist team members with the implementation of R/3

Benefits of ASAP Methodology

- The ASAP Methodology covers the entire project life cycle right from the initial evaluation via delivery and till post project management
- Proven and transparent approach that facilitates the project team to collaborate efficiently thus reducing implementation costs, time and risks
- Sensible risk management
- Better knowledge management wherein SAP solutions helps organize, implement and meet business objectives
- Steering committee tools and better communications planning
- Better results because ASAP methodology is based on the experience of others – the roadmap requires both soft skills and hard facts
- Project times are almost brought down to half
- Combination of all best practice tools including ITIL, PMI(Project Management Institute), Internal SAP and others

Introduction – ASAP Roadmap



In the following the roles and responsibilities within each phase of the ASAP roadmap will be described.

The implementation roadmap has six phases:

- | | |
|-------------------------------|---|
| 1. Project Preparation | The project is formally initiated, and planning is well under way. |
| 2. Business Blueprint | The project team gathers requirements and conducts the conceptual design of the solution. |
| 3. Realization | The solution is built, and the integration tested; performance tests are planned. |
| 4. Final Preparation | End users are trained; this is the final check before the cutover to the new system solution. |
| 5. Go Live and Support | The solution receives confirmation, ongoing support is in place, and the project is closing. |
| 6. Run SAP | The operability of the solution is ensured. |

Phase 1 - Project Preparation



Purpose

- Initial Planning and Preparation
- Define the project goals, scope and objectives
- Identify, on-board and train Team Members

Deliverables

- Project Scope Defined
- Implementation Plan & Rollout Strategy
- Detailed Scope Document
- Costs and Benefits Validation
- Project Standards
- Project Infrastructure
- Knowledge Transfer Approach
- Implementation Work plan
- Master Data Design
- Interface List
- Testing Strategy
- Data Cleansing Strategy

Milestones & Key Decisions

- Corporate Review Completed
- Scope Defined
- Project Team Staffed and Trained
- Project Team Organization, Responsibilities and Location
- Roll-out Plan Mandates/Constraints
- Policies for To Be Finance Organization
- System Retirement Objectives/Mandates/ Constraints
- Training Budget and Approach
- Key Stakeholders for Communications Identified
- Implementation Plan in Place


Activities in Project Preparation

- Defining the scope of Project
- Preparation of project plan
- Costs and Benefits Validation
- Implementation Work plan
- Master Data Design
- Interface List
- Testing Strategy
- Data Cleansing Strategy
- Team Preparation
- Client Interviews to the consultants if required
- SAP License related activities

Project Plan

BBP (25th Nov-21st Feb)	REALIZATION (22nd Feb-17th June)	FINAL PREPARATION (18th June- 24th June) CUTOVER PERIOD (20th June -24th June)	Go-Live & Hyper Care Support (25th June- 1st August)
•Kick off •As-Is •To-Be •BPD •GAP List •KDS	•Configuration •Unit Testing •Developments •Testing of upload programs • Uploading Master Data and Cutover Data in Quality System •SIT-System Integration Testing •Authorization Matrix •Key User Training •Creation of upload programs •UAT- User Acceptance Testing	•Upload of master data in Production •Upload of Cutover data in Production •Day to day entries in Production •End User Training by Key Users	•Official first transaction in Production system •Hyper Care Support

Phase 2 - Business Blueprint

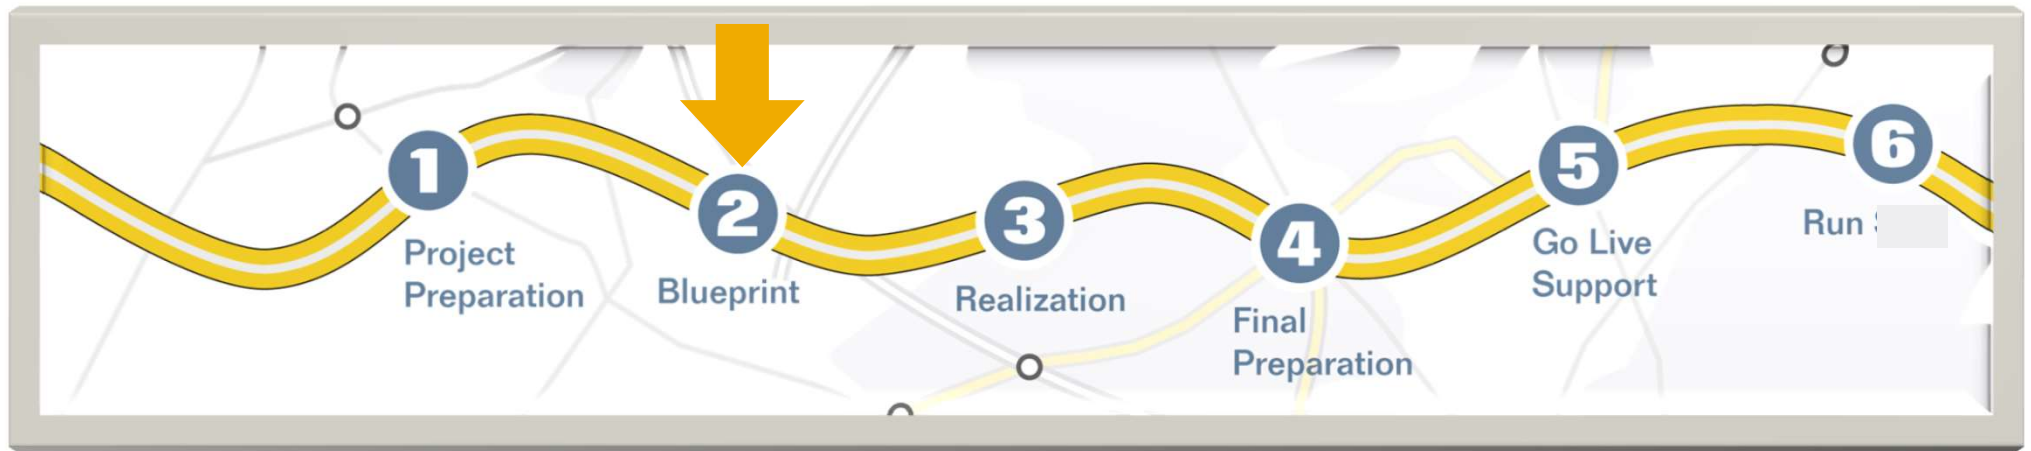

Purpose

- To create a body of work, known as Business Blueprint that
- Aligns business requirements to the SAP business model
 - Documents the TO-BE process models
 - Describes the solution design
 - Identifies additional functional and technical requirements
 - Obtains business sign-off on requirements and design
 - Blueprinting is dedicated to support value delivery

Deliverables

- Project Plan Update
- Complete, documented and signed off
 - Business Process Hierarchy and Design
 - Value Association on Process Level
 - Solution Design
 - Gap Identification and Resolution
 - Solution Landscape and Architecture
- Assessment of Organization and Business Process Changes
- Confirmation of Implementation Date

Milestones & Key Decisions

- Completed and signed off Process Design
- Completed and signed off Solution Design
- Completed and signed off gap identification and resolution
- Phase Quality Assessment
- Communication Plan

Activities in BBP Phase

- This phase starts with Kick off meeting
- Kick off meeting is useful to give a kick start to the project and also give an overview on project plan and future activities
- Attendees for Kick off meeting

IT Team	Client Team
▪ Accounts Manager ▪ Project Manager ▪ Consultants	▪ Higher Management ▪ Project Manager ▪ Process Owners ▪ Core Team members

- After kick off meeting, discussions or Question & Answers sessions will be started on As-Is process to understand the current business processes

Activities in BBP Phase

- To Be process documents are prepared as per As-Is discussions
- Level 0 Training
- Business walk through presentation (Level 1 training) will be given to all the process owners and core team members
- As per the inputs and corrections from the client, Business Blue print documents are changed and share the copies to the client
- BBP documents have to be signed off from the client
- Key Data Structures(KDS) document has to be prepared and signed off
- GAP list has to be identified and required solutions have to be proposed
- As per the new developments, ABAP consultants are nominated for the project
- All the templates and sample documents are given below



As-Is process.xlsx



Document



KDS_MM_Templa
te



GAP Analysis

Roles of Consultants in BBP/BPD Phase

Functional Consultant:

- Participating in Kick off meeting
- Participating in Business As-Is discussions
- Asking questions about process and prepare rough To Be processes
- Preparing Blueprint Walkthrough presentation and giving presentation to Process Owners and Core Team Members
- Preparing Blueprint Documents
- Updating Blueprint Documents as per business review
- Discussion about Material Number range, Material types, PR document types, PO Document types , number ranges
- Preparing KDS as per the discussions
- Preparing Gap List to find out required developments

Technical Consultant:

- No major involvement

Phase 3 - Realization



Purpose

- Build and Test a Complete Business and System Environment
- Develop Training Material and End User Documentation
- Obtain Business Approval


Deliverables

- Test Data and Configuration
- Business Process Procedures
- Quality Assurance System Environment
- Production System Environment
- Develop and Test Interfaces, Conversions and Reports
- Evaluate and Enhance Security and Controls
- End-User Training Material and Plan
- End-User Training System Environment
- Data Conversion Plan
- User Acceptance Test

Milestones & Key Decisions

- Project Team Trained (Realization)
- Final Design and Configuration
- Integration Test
- End-User System Infrastructure
- User Acceptance
- Phase Quality Assessment
- Readiness Review

Landscapes in SAP

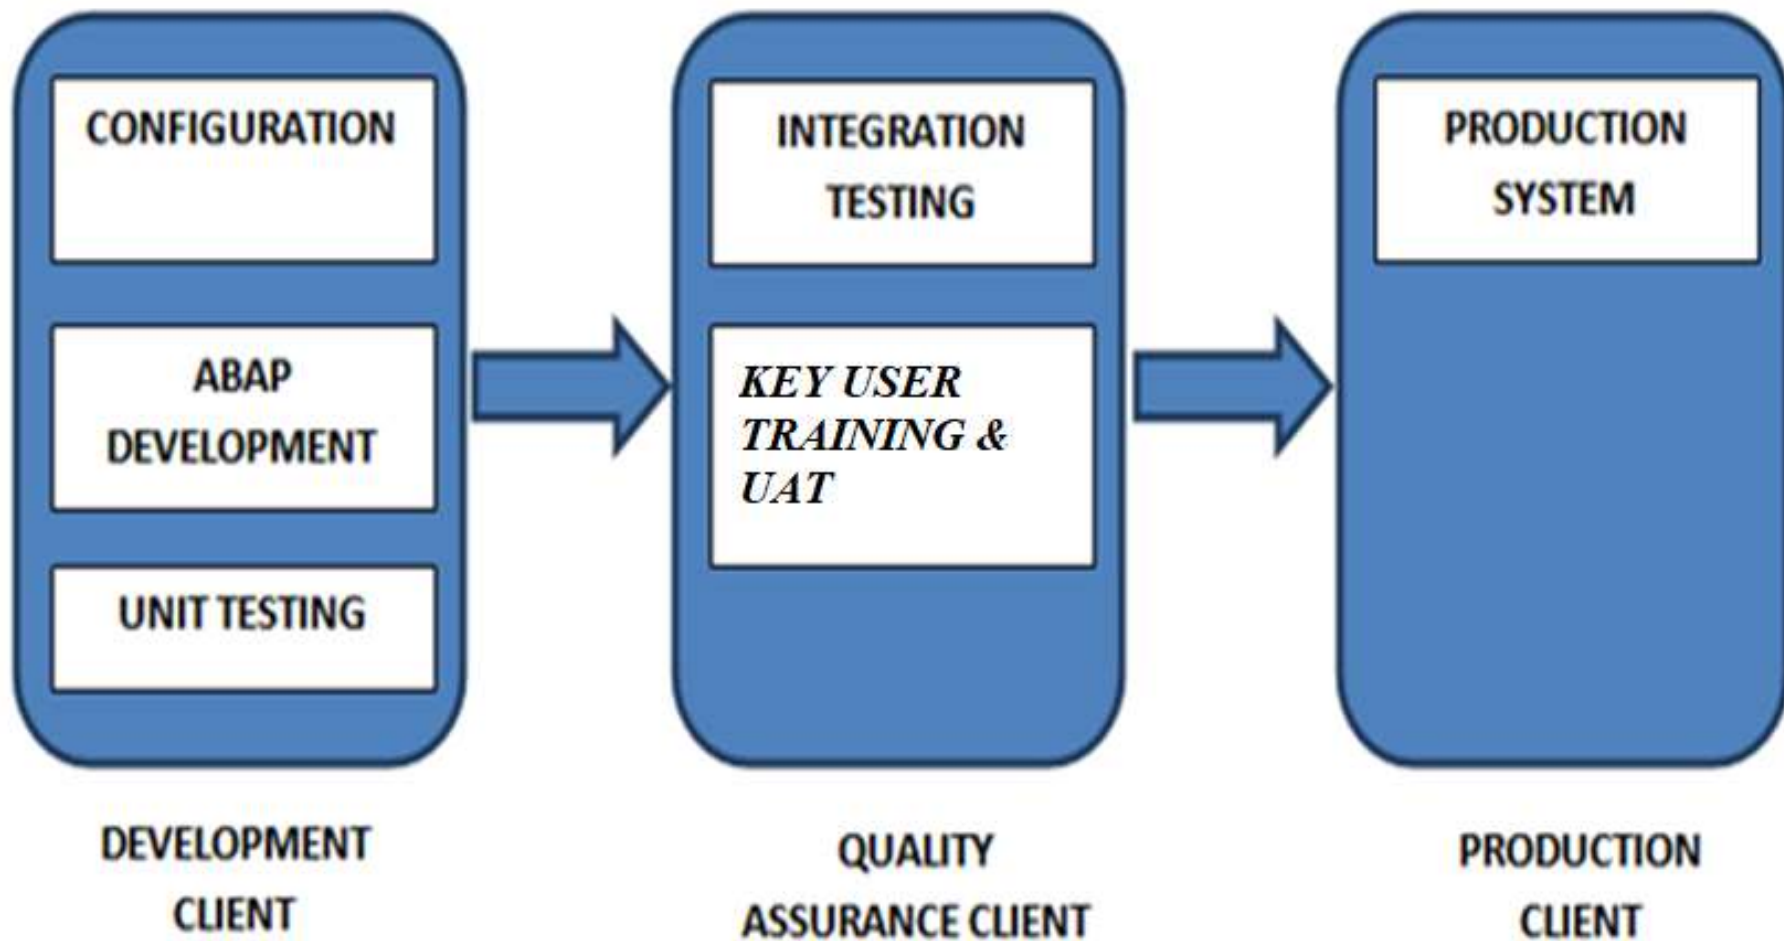

Activities

- Once server is received, system must be verified and required nodes need to be activated
- Configuration of Enterprise Structure and other processes
- Creating master data for Unit Testing
- Unit Testing in Development system
- Releasing of Transport requests to Quality system
- Cleansing of Master Data and Test Upload Programs
- Upload Master Data (Material, Vendor, Purchase Info record, Source List)
- System Integration and User Acceptance Testing in Quality System
- Developing Smart forms, Reports, Enhancements etc.
- Testing of new developments and developments must be signed off from client
- Detailed Level 2 training to Core Team members
- Upload Master Data (Maximum data will be given by client)
- Supporting Key Users for UAT

Templates of UT, SIT and FS

UT Template:



UT Template

SIT Template:

Same template is used to for testing like System Integration Testing and User Acceptance Testing. UAT is also called as Final Acceptance Testing and Business acceptance Testing



SIT Template

Functional Specification (FS) sample:



FS-Domestic
Purchase Order

Roles of Consultants in Realization


Functional Consultant:

- Configuration in Golden/Configuration client
- Doing Unit Testing in Testing Client under development landscape
- Preparing Functional Specifications and coordination with Technical consultants
- Testing of Developments
- Testing of Upload Programs
- Preparing Test Scripts
- Doing System Integration Testing (SIT) in Quality system
- Prepare Training Material and Provide Training to Core Team members
- Giving support to User Acceptance Testing (UAT or FAT)

Technical Consultant:

- Understand the list of developments as per the GAP list
- Understanding the FS and developing as per the requirement
- Coordinating with Functional consultant to meet the client's requirement
- Preparing Technical Specification

Phase 4 - Final Preparation

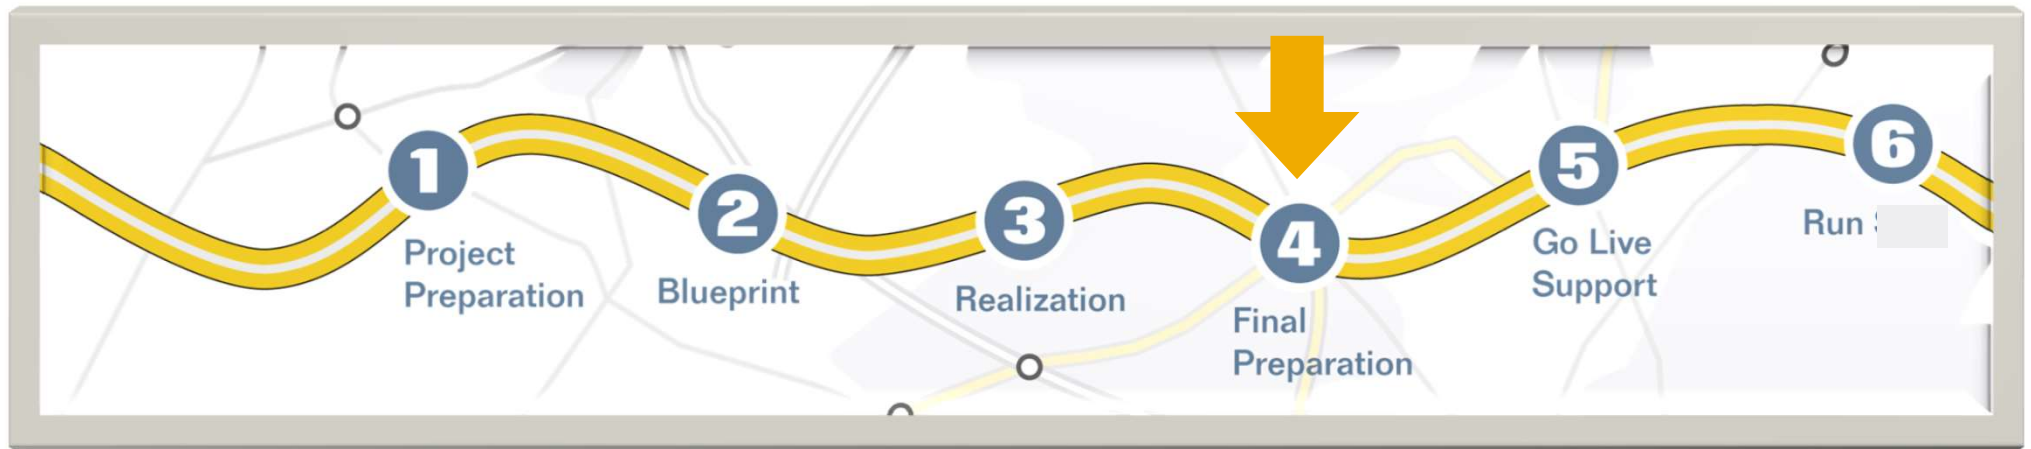

Purpose

- Prepare System for Production Release
- Prepare the Internal and External Organization for Go-Live

Deliverables

- Data Converted
- Cut-Over Plan
- End-Users Trained
- End-User System Ids Created
- System Support Organization in Place
 - Help Desk
 - Technical Support
- Operational Production System Environment

Milestones & Key Decisions

- Organizational Changes Implemented
- Go/No-Go Decision

Activities in Final Preparation

- Final Master Data upload with Data Migration programs in Test System
- **End User Training – Can be given by Key Users with the support of Consultants or Consultants only give the Training**
- Collecting Master data and Cutover data from business
- Migrating the Master data and Cutover data to SAP production system from non legacy systems
- Creation of User IDs for End users
- Providing authorizations to the users as per the requirement

Templates of data migration programs and Authorization Matrix:



Material Creation Template.xlsx



Open PO.xlsx.xlsx



Roles and Authorization.xlsx

Cutover Data

MM Cutover Data:

- Open Purchase Orders
- Open Work Orders (Service Purchase Orders)
- Open Stock

FI Cutover Data:

- Open Payments
- Vendor Balances
- Customer Balances
- Vendor Advances
- Customer Advances

SD Cutover Data:

- Open Sales Orders
- Open Billing
- Open Contracts

Roles of Consultants in Final Preparation


Functional Consultant:

- Identifying the cutover data and testing the upload programs in Quality system
- Uploading Master data in Production System
- Uploading Cutover Data in Production System
- Working to complete the activities within cutover period as per the plan
- End User Training
- Documentation of all the phases

Technical Consultant:

- Completing the pending developments as per the plan
- Preparing Technical Specifications
- Creating the upload programs for cutover data
- Coordinating with functional consultant

Phase 5 - Go-Live and Support

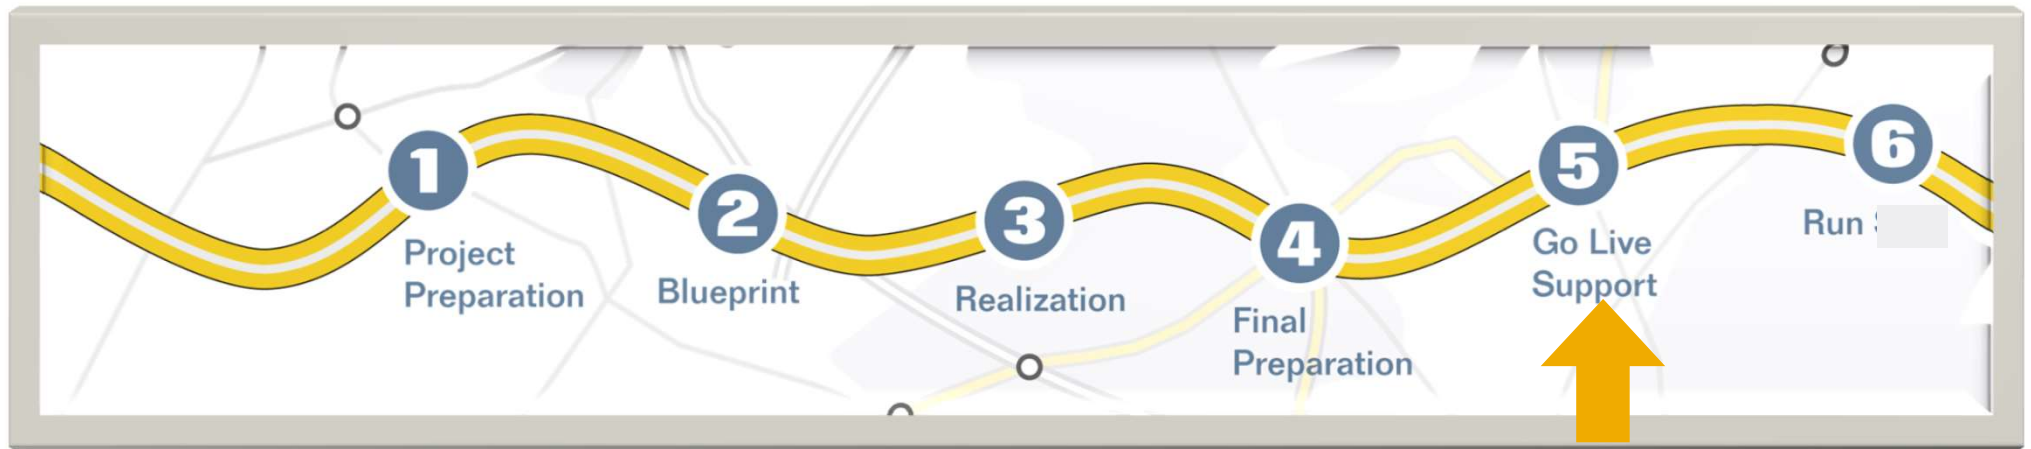

Purpose

- Business Owns and Executes New Business Processes and Systems
- Monitor Business Process Results
- Monitor Production Environment
- Establish Center of Excellence for Support and Enhancements

Deliverables

- Live Production Environment
- Operational Help Desk
- Cut-Over and Conversion Activities Completed
- Post Go-Live End-User Training
- Updated Business Case
- Lessons Learned

Milestones & Key Decisions

- Go-Live
- Project Close

Activities in Go-Live & Support

- Resolution of tickets on day to day basis
- Monitoring initial tickets
- Handover of project to support team

Roles of Consultants in Go-live & Support


Functional Consultant:

- Once the Go-Live is happened, initial support has to be given
- Handover to Support Team
- Changes in configuration as per the requirement
- Later support activities will be taken by support team

Technical Consultant:

- Completing pending developments
- Modifications to existing developments as per the requirement
- Preparing Technical Specifications

Phase 6 – Run SAP

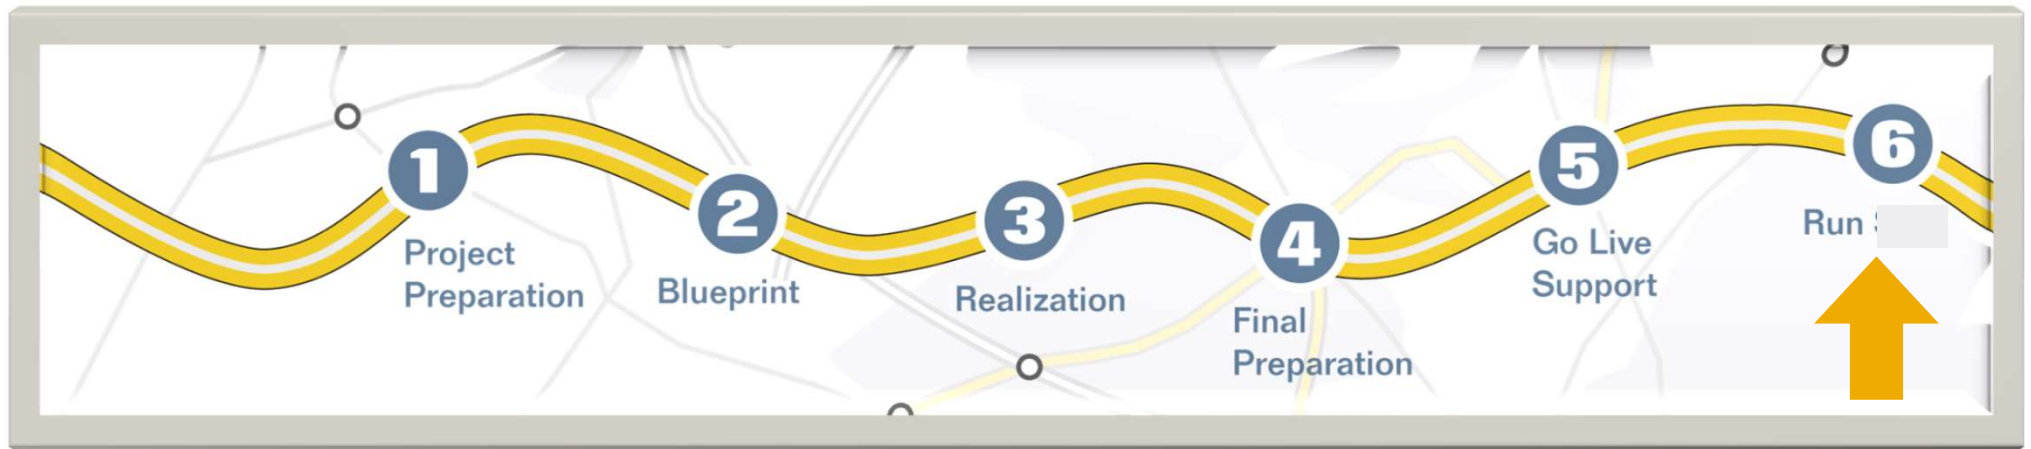

Purpose

- Run implemented SAP solution
- Optimize solution operation by implementing SAP Operation standards

Deliverables

- Assessment of Operation Standards for optimize solution operation
 - Identify scope
 - Setup project schedule for implementing
- For each relevant Operation Standard
 - Design of processes, organization and roles, blueprint for tool usage
 - Setup of processes, organization and roles, tool setup
 - Transition into production incl. training and rollout
 - Operating

Milestones & Key Decisions

- Identification of Operation Standards for optimize solution operation
- Design, Setup and Operation of SAP Operations Standards
- Tool implementation (mostly SAP Solution Manager scenarios for operation)

Activities in Run

- Resolution of tickets as per Service Level Agreements
- Monitoring tickets in supporting tool such as Solution Manager/HPSM/Remedy/ITMaas etc.
- Proper documentation of Service requests and Change requests
- Development of new customized tasks as per the business requirement
- Meetings on status of support tickets

Roles of Consultants in Run SAP

Functional Consultant:

- Handling tickets as per the Service Level Agreement(SLA)
- Preparing functional specifications for new developments
- Analyzing the tickets and changing configuration as per the requirement
- Giving End user trainings as per the requirement

Technical Consultant:

- Working on new developments as per the requirement
- Working on existing changes in developments
- Working on any technical or coding related tickets

